



These are the latest photographs of the progress at the construction site, to give you an insight into the work that has been completed in the last month. **We value your trust in CNTC Hong Kong and thank you for your support.**

1. Podium Driveway



2. View from back gate



3. Model Flat in progress



4. Block work update till 9th floor



2nd to 3rd floor
(Plastering work)



4th to 6th floor
(Block work completed)



7th to 9th floor
(Block work WIP)

5. Laying of Electrical Conduent on 24th floor



6. View of Block A



7. View of Block B



8. Front view



9. Top view



10. Side view



CONSTRUCTION PROGRESS SEP 2018 - NOV 2019



Sept 2018 - 2nd floor slab



Oct 2018 - 3rd floor slab



Nov 2018 - 4th floor slab



Dec 2018 - 6th floor slab




Jan 2019 - 7th floor slab



Feb 2019 - 10th floor slab



Mar 2019 - 11th floor slab

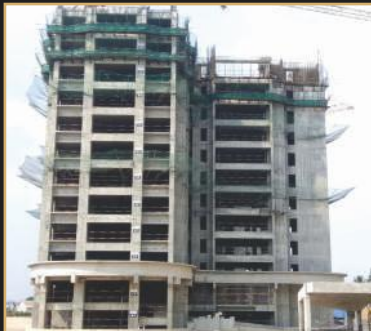

Apr 2019 - 12th floor slab



May 2019 - 13th floor slab



Jun 2019 - 16th floor slab



Jul 2019 - 18th floor slab




Aug 2019 - 20th floor slab



Sep 2019 - 20th floor slab



Oct 2019 - 22nd floor slab

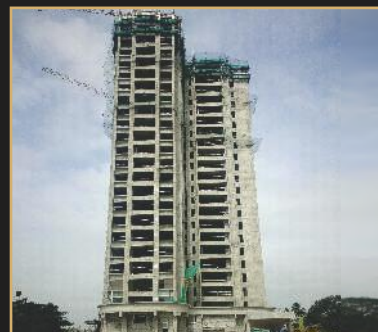

Nov 2019 - 24th floor slab

Drone Shoot View



**THE
PRESIDENTIAL
TOWER**



The Presidential Tower

No. 8, Tumkur road, Near The Taj, Yeshwanthpur, Bengaluru - 560022.

Ph. +91 96861 07178 | www.cntcindiaprojects.com

RERA Registration No. PRM/KA/RERA/1251/309/PR/171014/000565
